

17 Cost and Schedule Summary

The overall LZ Project plan is summarized in this chapter, including an overview of the Project schedule and the concept for the division of scope and cost among the various funding sources. The planned contributions supported by DOE, South Dakota Science and Technology Authority (SDSTA), the UK's Science & Technology Facilities Council (STFC), China, Portugal, and Russia are outlined. This is a joint project with an international collaboration, and the cost-accounting approaches differ. Therefore, we have attempted to utilize the U.S. DOE cost-accounting approach for the costs presented in this chapter.

17.1 Project Schedule

The goal is to begin commissioning and early operations by the start of 2019. The key assumptions behind this date are the timing of the initial CD reviews and the date when we can begin procuring long-lead items such as low-background phototubes for the TPC.

The early critical decision milestones in this plan are a DOE CD-1/3a review in March 2015, followed by a CD-2/3b review in early 2016. Assuming successful reviews and approvals, this enables procurement of long-lead items as early as the late spring of 2015 (by the UK, other) and letting contracts for many other items in early 2016. By late 2017, we should be ready to begin assembling the Xe detector elements into the inner cryostat in the upgraded clean-room assembly space in a surface laboratory at SURF. In parallel with this, decommissioning and removal of the LUX detector will take place. A more complete view of the project schedule is shown in Figure 17.1.1. The dates shown in this schedule correspond to early-finish milestones. Critical decision milestones are given in Table 17.1.1. The future milestones in Table 17.1.1 include schedule float and thus are not indicative of early-finish milestones.

LZ Summary Schedule

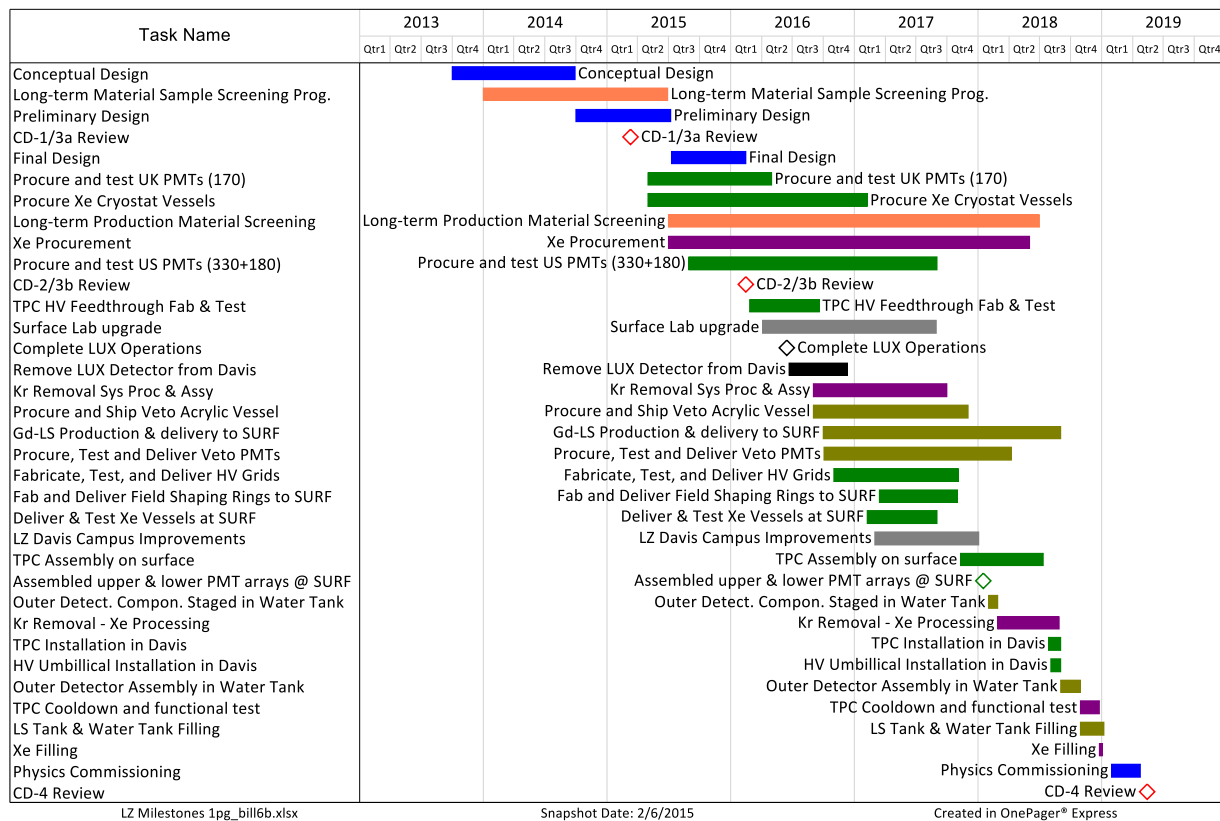


Figure 17.1.1. Summary of LZ schedule. The dates are in calendar-year quarters, not fiscal-year quarters.

Table 17.1.1. Key Project critical decision milestones (U.S. fiscal quarters). Schedule float is included in the future milestones. These are not early-finish dates.

Level 1 Milestone	Schedule
CD-0, Approve Mission Need	9/2012 (actual)
CD-1/3a, Approve Alternative Selection, Cost Range & Long-lead Procurement	May 2015
CD-2/3b, Approve Performance Baseline & Start of Construction	Q3 FY 2016
CD-4, Approve Project Completion (Ready for Data Taking)	Q1 FY 2021

17.2 Project Scope

The Project’s entire technical scope has been described in the previous chapters. The complete LZ Project includes the detector elements — purified Xe, cryogenic systems, Xe detector, cryostat, veto system, calibration system, electronics, DAQ, trigger, online and offline software, as well as all the integrating activities — system tests, system integration, assembly/installation, on-site infrastructure, and project management.

The planned scope division among the various U.S. and non-U.S. agencies is summarized briefly here. The project scope will be finalized when a formal agreement is completed and approved by the federal, state, and non-U.S. funding agencies.

The major elements of UK scope deliverables include about one-third of the low-background PMTs for the Xe detector, the cryostat set (inner and outer), elements of the low-background counting capability, contributions to integrated system tests, the source calibration delivery mechanism, and extensive contributions to computing and software.

Portugal is expected to contribute to control systems, software, and a measurement system for TPC quality control.

Russia is expected to contribute Xe, and to contribute to integrated system testing and diagnostics.

China may also contribute Xe, possibly including Kr removal, and may contribute to TPC systems, computing, and software. Chinese institutions are not yet members of the LZ collaboration but are starting to be involved in technical and other meetings.

The SDSTA scope includes above- and belowground modifications to required facilities and, as a goal, much of the Xe needed for the experiment.

The NSF is assumed to support scientific efforts for those U.S. collaborating institutions funded by NSF but will not contribute to the Project scope.

The DOE is assumed to fund all remaining Project scope.

17.3 Cost Summary

The U.S.-based cost estimate associated with the above scope is shown in Table 17.3.1 in at-year dollars.

Table 17.3.1. LZ Project U.S.-equivalent cost in at-year dollars. The columns show the DOE base cost (without contingency), planned U.S. equivalent costs of non-U.S. in-kind contributions, the equivalent cost of in-kind contributions planned from SDSTA, DOE contingency, other contingency (from non-U.S. or SDSTA), and the total U.S. equivalent costs.

WBS / TASK NAME	DOE Base	Foreign	SDSTA	DOE Cont.	Other Cont.	TOTAL COST
1.1 Xe Procurement		6,060,000	14,140,000			20,200,000
1.2 Xe Vessel		1,937,445			416,000	2,353,445
1.3 Cryogenic System	1,483,450			465,926		1,949,376
1.4 Xe Purification	5,782,541	247,582	279,924	2,017,761		8,327,808
1.5 Xe Detector System	7,478,267	2,706,965		2,279,357		12,464,589
1.6 Outer Detector	3,961,426	225,865		1,230,873		5,418,164
1.7 LZ Calibration System	600,621	93,580		180,186		874,387
1.8 Electronics, DAQ, Controls & Computing	3,311,935	151,065		970,947		4,433,947
1.9 Integration and Installation	3,504,935		1,252,800	1,057,582	300,000	6,115,317
1.10 Cleanliness and Screening	1,214,661	822,926		353,250		2,390,837
1.11 Offline Computing	2,127,320	399,176		638,195		3,164,691
1.12 Project Management	3,222,607			930,285		4,152,892
Risk Based Contingency				4,652,000		4,652,000
TOTAL COST	32,687,763	12,644,604	15,672,724	14,776,362	716,000	76,497,453
