

13 Infrastructure at the Sanford Underground Research Facility

This section describes the SURF surface and underground infrastructure improvements and additions needed in order to facilitate the assembly and installation of LZ. A detailed assembly and installation sequence for LZ is presented in Chapter 14. Infrastructure at SURF includes the following items: (a) surface laboratory space for assembly of the Xe detector (WBS 1.5) into the inner cryostat vessel (WBS 1.2); (b) staging space for scintillator veto tanks and scintillator (WBS 1.6), for the outer cryostat subcomponents (WBS 1.2) and other detector components; (c) secure storage space for Xe; (d) custom tooling for lowering the fully assembled Xe detector sealed inside the inner cryostat down the Yates shaft; and (e) modifications to the Davis Campus at the 4850L of SURF. These infrastructure elements are described in the subsections below. Surface and infrastructure improvements will be funded by the South Dakota Science and Technology Authority (SDSTA). The design of the infrastructure improvements will be a joint effort of the SDSTA engineering and technical staff and the LZ collaboration.

13.1 Surface Infrastructure

The principal components of the surface infrastructure specific to LZ are: (a) the Surface Assembly Laboratory (SAL); (b) the Surface Storage Facility (SSF); and (c) office and meeting space at the SDSTA administration and education buildings. Office and meeting space already exists for ongoing experiments at SDSTA; general improvements to these capabilities will serve the broader experimental community at SURF, and are not described here. The locations of the SAL and the SSF at SURF are shown in Figure 13.1.1.



Figure 13.1.1 Aerial view of the SURF site showing the locations of the Surface Assembly Laboratory and the Surface Storage Facility.

The SAL was utilized for the assembly of the LUX detector (Chapter 5) and for operation of LUX in a water tank located in the SAL. Significant upgrades to the SAL are planned for assembly of the LZ detector and are described later. The most significant improvement to the SAL is the addition of radon-reduced air-handling capability. The SSF is currently used for general storage. Modest improvements are needed for the SSF.

13.1.1 Surface Assembly Laboratory (SAL)

The SAL building is a wood-frame structure comprising four levels: the surface level and levels -1, -2, and -3, which are successively deeper below the surface. This building was renovated for LUX assembly and testing and has a current sprinkler system, new HVAC, and 220 kVA installed electrical capacity. An existing clean room of 2,900 ft³ will be used for cleaning and staging of metal parts and bagged PTFE parts prior to Xe detector assembly in the low-radon clean room. A new low-radon clean room will provide workspace beneath an existing monorail and over a pit in Level -1. New floor supports will support the assembly of the inner detector. Transport of the detector will be facilitated by rolling it to the building shipping dock. The layout of the SAL is shown in Figure 13.1.1.1.

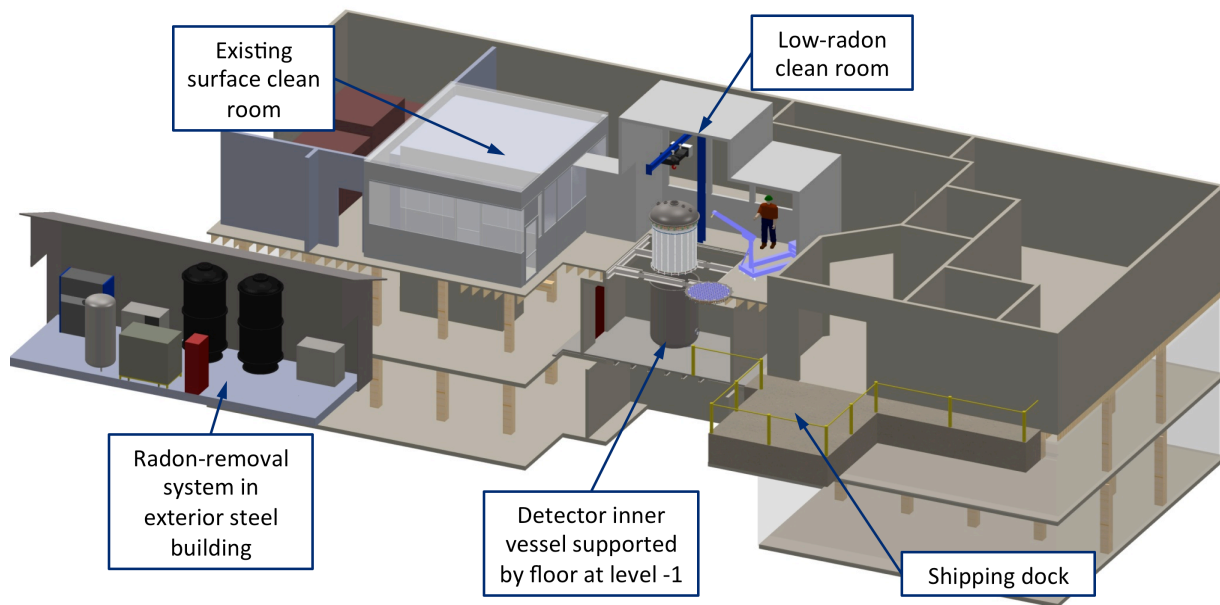


Figure 13.1.1.1. The Surface Assembly Laboratory.

13.1.2 Radon-reduced Air System

Radon is one the highest-risk contaminants for low-background experiments because it can easily escape from bulk material and quickly diffuse into active parts of the detectors. The innermost materials and parts of ultralow-background experiments must be manufactured or assembled in a radon-suppressed atmosphere. Final assembly of the LZ TPC will occur in a clean room in the SAL, which has a radon-reduced air system.

Carbon adsorption is the preferred technique for removing radon from air and has been effective for varying degrees of radon contamination, from as low as a few mBq/m³ for low-background experiments to levels as high as ~100 Bq/m³. The radon level at the surface at SURF is expected to be in the range of ~20 Bq/m³. The LZ detector assembly clean room will be designed with a radon-reduction factor of greater than 1,000. It will be flushed with radon-reduced air at a flow-rate of 300 m³/h, which is produced by compressing, drying, cooling, and pushing the air through two 1,600 kg activated-carbon towers. Our baseline plan is to use commercial units provided by ATEKO, which has recently developed and built

large commercial radon-removal systems for the Cryogenic Underground Observatory for Rare Events (CUORE) and Borexino experiments. These units are capable of reducing radon concentration in the air by a factor of greater than 1,000.

The proposed system is similar to that used by CUORE. A preliminary quotation from ATEKO has been obtained. Discussions to adapt the design to SURF requirements have been held and a site visit made to ATEKO in the Czech Republic. The process is based on compression, cleaning, and drying (dew point -65°C min.) of air, cooling to -55°C , adsorption of radon from air on activated carbon at -50°C at approximately 8 bars of pressure, followed by heating and pressure reduction of air to ambient pressure and temperature. The system requires a space of about 4.5 m x 7 m with a height of 3.2 m (absorbers with frame). The components of the proposed system from ATEKO are illustrated in Figure 13.1.2.1. Most of this system would be located outside the SAL and will be procured by SDSTA.

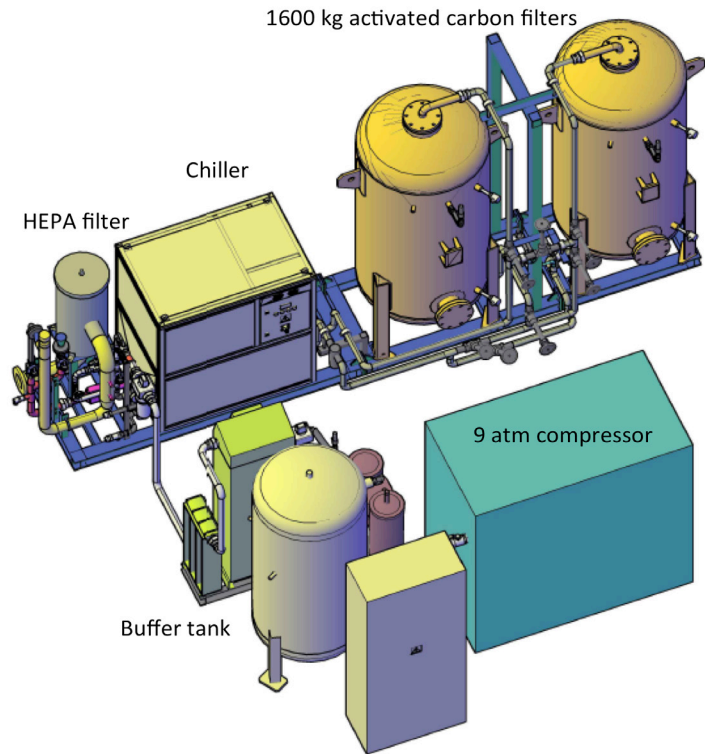



Figure 13.1.2.1. Typical component layout for a radon-removal system from ATEKO. The total weight of the system is approximately 5,500 kg. Each carbon column weighs 1,600 kg.

13.1.3 Surface Storage Facility (SSF)


Short-term storage and staging of equipment needed for experiment assembly will be facilitated by upgrades to an existing building next to the SAL. This includes the large scintillator tanks. The SSF has a large high bay with approximately 445 m² (4,800 ft²) of lay-down space under a 40-ft-wide 10-ton bridge crane. Hook height on the bridge crane reaches 7.3 m (24 ft). Handling of equipment will also be facilitated by three wall-mounted jib cranes rated at 1 ton, 2 tons, and 3 tons, respectively. Truck entry to the building is via a 4-m (13-ft)-wide x 5-m (16-ft)-tall entry rollup door. Temporary heaters will probably be needed to heat some of the space in this building during the winter months.

13.2 Yates Shaft Infrastructure and Custom Transport


The LZ TPC inside the inner cryostat will be transported from the SAL to the Yates headframe in a horizontal orientation. The transport method will be similar to the successful transport of LUX from the same building to the headframe. A large telehandler was used, along with continuous monitor of orientation and G-forces. LUX was transported in the Yates cage but the LZ assembly will be slung under the cage, given its larger size. The LZ detector/inner cryostat will be placed on a custom transport frame. Once the detector/inner cryostat assembly arrives at the Yates headframe, the assembly on the transport frame will be lowered in the Yates shaft as shown in Figure 13.2.1. Lowering the assembly on its transport cart slung under the Yates cage will take some hours. A crew member will accompany the assembly in the Yates conveyance as was done for LUX. The assembly and transport cart will be extracted from the Yates shaft at the 4850L and rotated back to the horizontal orientation.

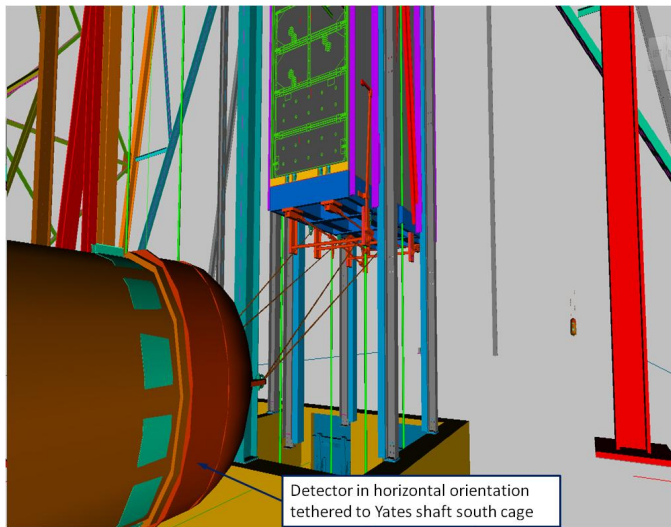

In the first image, the LZ detector lies horizontally at the shaft entrance and the cage bottom is 6 to 7 feet above the floor. Crews will cover the shaft by installing a work platform and attach the slings to the bottom of the cage. These are also attached to the top of the LZ detector. The platform will be removed and the cage hoisted to remove slack. Another wire rope control line from a winch is attached to the bottom of the detector.

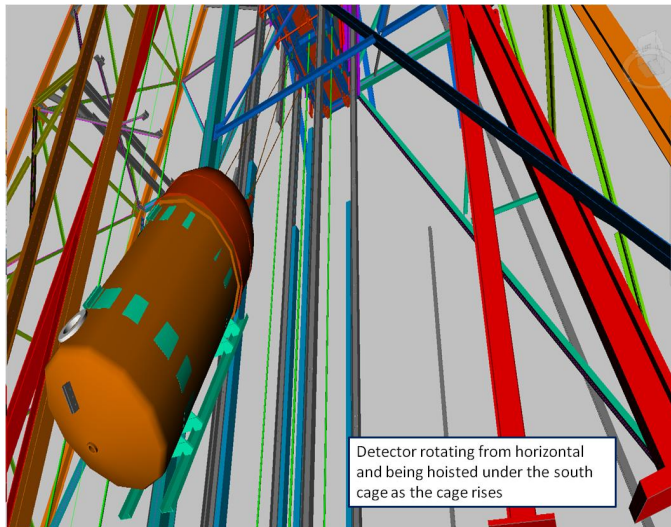

In the second image, the hoist is lifting the LZ detector in the shaft to its vertical position. The control line mounted on the detector bottom will maintain tension in order to control the swing into the shaft. Even though not fully in the shaft, the bottom of the custom transport frame is off the ground. Once hoisting is in process, it will not be stopped unless a difficulty arises. The entire procedure is short-lived.

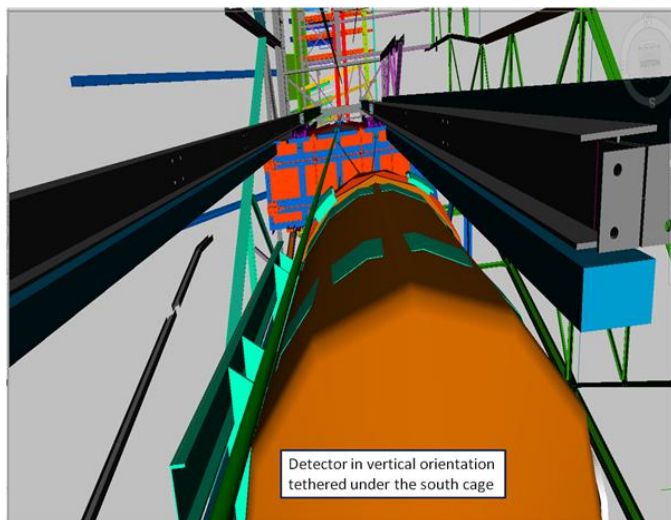

In the third image, looking almost vertically. Here, the detector is hanging vertically. It will be positioned properly in order for the crew to attach the bumpers or guide shoes for clearance and centering during shaft transit. After inspections, a crew will man the cage and watch as it travels underground, being lowered at a rate of 0.7 ft/sec.

Figure 13.2.1. The transport method of the LZ TPC inside the inner cryostat will be similar to the successful transport of LUX from the same building to the headframe.

13.3 Underground Infrastructure

A plan view of the Davis Campus is shown in Figure 13.3.1. After arriving on the 4850L, the detector will be transported to the Davis Cavern via the Primary Access Drift, passing by the room housing the MAJORANA detector, as depicted in Figure 13.3.1. That is the same access-way utilized for transport of the LUX detector. The larger LZ inner cryostat can be moved through the same space by temporarily removing short segments of the Davis Campus HVAC air-supply ducts to allow for sufficient clearance. All access doorways are sufficiently large to allow for detector passage. Entry to the Davis Cavern via the Primary Access Drift allows the transporter design to take advantage of the 8,100-lb maximum floor loading afforded by design of the Davis Cavern structural steel. It would also be possible to transport the inner detector in the drift that passes by the LN storage room, but this would require the removal (and later replacement) of a wall between the drift and the Davis Cavern.

LZ will take advantage of design features built into the Davis Cavern to allow for deployment of a larger detector than LUX. A 102-inch-diameter flange is built into the 70,000-gallon water tank. Additionally, the redundant 50-ton water chillers and the Davis Campus 1500 kVA substation were implemented with a large future detector in mind.

Figure 13.3.2 shows an isometric view of the LZ deployment in the Davis Campus. Xenon storage cylinders will be securely deployed in a newly upgraded portion of the LN storage room access drift (shown in the lower-right-hand corner). Currently, this is an unfinished area that has been used for rock-moving equipment / storage. SURF will upgrade this area by providing concrete floors and shotcrete-covered walls while also closing off the space to allow for flow-through ventilation. Ventilation will be adequate to mitigate potential oxygen deficiency hazards that could occur in the event of a release from one of the Xe storage cylinders. The Xe cylinders are more thoroughly described in Chapter 9.

The LN storage rooms and control rooms will be largely reused as they were for LUX. LZ will utilize a similar scheme for LN storage tanks until a second cryocooler is secured for long-term operational flexibility. These tanks will supply makeup nitrogen to the cryocooler, assist with transient startup effects, purge gas for the water purification system, and provide some buffer against short-term power interruptions. The control room is expected to remain unchanged, providing minimal office space for underground workers during assembly, commissioning, and data taking.

The size of the ventilation duct that exhausts the LN storage room will be increased to allow for the added flow-through ventilation needed to include the Xe storage.

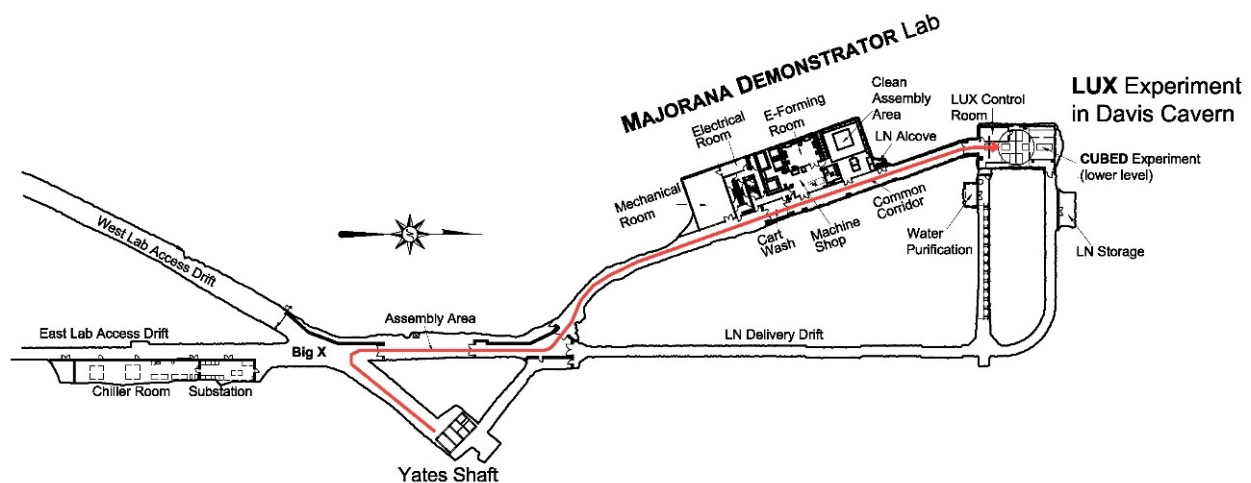


Figure 13.3.1. Plan view of the Davis Campus at the 4850L.

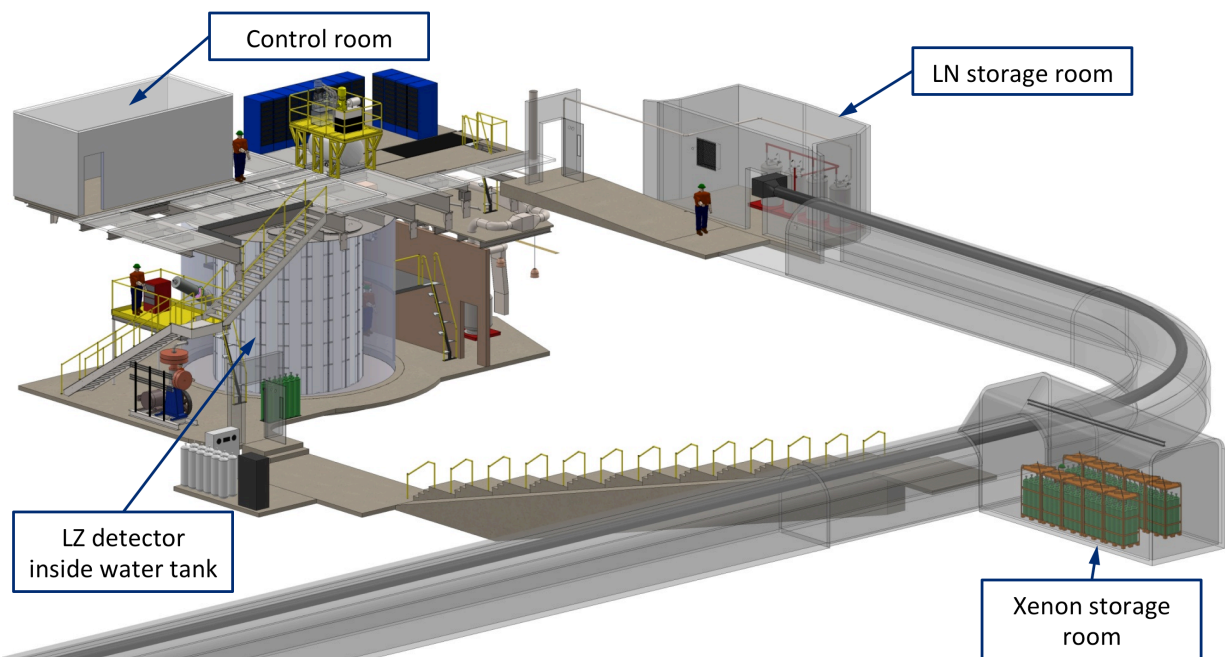


Figure 13.3.2. Overall layout of LZ in the Davis Campus

Figure 13.3.3 depicts a close-up view of the Davis Cavern showing supporting infrastructure installed. Key elements include data acquisition (DAQ) cabinets, a Stirling cycle cryocooler to support cooling thermosyphon lines, a platform for a high voltage (HV) power supply, a Xe compressor installed below the steps accessing the lower Davis Cavern, another platform that interfaces to the Xe purification tower, and Xe circulation / storage equipment deployed both in and above the current low-background counting rooms in the lower Davis Cavern.

To facilitate deployment of a larger number of DAQ racks and cryocoolers on the deck of the upper Davis Cavern, SURF will decommission and remove the existing clean room to open up floor space. Platforms deployed near the HV feedthrough and Xe purification tower will also serve to significantly increase the effective floor space in the cavern.

This positioning of the Xe compressor within the cavern places this large piece of 480 V equipment closer to in-cavern existing power panels, while also positioning it to the low-pressure / higher-loss suction side of the Xe gas system. All other Xe circulation and storage equipment take advantage of being co-located in space behind block walls previously utilized for low-background experiments.

The Davis Campus is fed from a 1500 kVA substation. The substation is presently loaded at approximately 60% during worst-case conditions, and has ample reserve capacity to accommodate the projected LZ electrical load of 146 kW (an increase of ~100 kW from LUX) (summarized in Chapter 11). The campus has a 300 kW emergency generator that supplies the air-handling systems, communications, facility control and alarm systems, and egress lighting for up to 48 hours. Floor space is available for an additional 50-100 kW generator to provide backup power for experiments.

To reduce the risk of radon exposure during assembly sequences of the detector inside the water tank, radon-reduced air from the SAL will be plumbed to the assembly area in a pressurized 2-inch pipe installed in the Yates shaft. This takes advantage of the 8-bar discharge pressure of the radon-reduction system to minimize the size of required piping through the shaft and to the Davis Campus. Further study may indicate that the radon content of surface air is sufficient during the short times the sensitive detector components are exposed to air in the water tank. If so, then some small cost reduction will be possible but

a dedicated pipe from the surface would still be required. The radon levels in the Davis Campus are 20 times or more larger than at the surface.

The water tank installed for the LUX experiment was designed to be able to accommodate a much larger experiment. The modifications required for LZ are modest.

The pads that support the LUX detector will be removed from the tank floor. Mounting plates will be added to the tank floor for the LZ detector and mounting points for the four side scintillator vessels. At larger radius, mounting points will be installed for the 20 PMT ladders. In addition, a support for the lower conduit that connects the detector to the LXe tower and PMT cable breakout will be installed. Finally, a support for the HV feedthrough will be added.

The detector HV system for LZ requires a feedthrough in the wall of the water tank. In addition, a penetration of the tank wall is needed for routing of the conduit that connects the detector to the LXe tower and the PMT cable breakout. A neutron tube will be installed for the neutron calibration system, and that tube will be filled with water for normal running and nitrogen for calibration. The top of the water tank will have several feedthroughs to accommodate thermosyphons, detector cables, source tubes, scintillator lines, water PMT cables, LED flasher cables, and vacuum pumping.

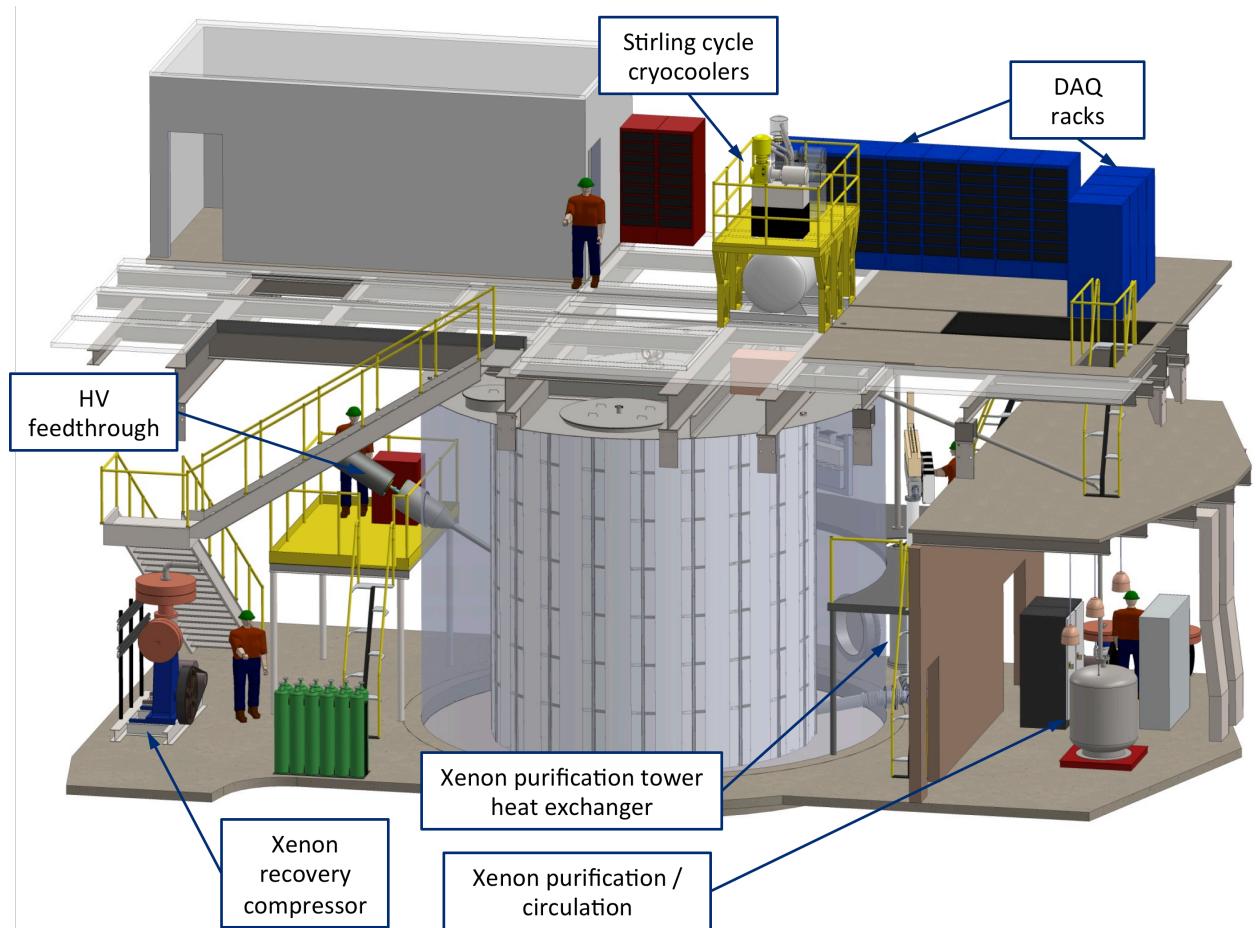


Figure 13.3.3. LZ and related support systems in the Davis Cavern.
