













CROWBAR

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Feb 2, '03							Feb 9, '03				
							F	S	S	M	T	W	T	F	S	S	M	T
1	Circuit Design	10 days	Fri 1/31/03	Thu 2/13/03		Sam[50%]												
2	Board Manufacturing	7 days	Tue 2/18/03	Wed 2/26/03	1													
3	Fabricate First Unit	1 day	Thu 2/27/03	Thu 2/27/03	2	Sam												
4	Test First Article	1 day	Fri 2/28/03	Fri 2/28/03	3	Sam												
5	Order Parts	2 days	Wed 2/19/03	Thu 2/20/03	1													
6	Parts Delivery	5 days	Fri 1/31/03	Thu 2/27/03	5													
7	Machine Panels	2 days	Fri 1/31/03	Mon 3/3/03	6	Physics Shop												
8	Board Assembly	6 days	Thu 2/27/03	Fri 3/7/03	6,2	LuAnn												
9	Final Assembly	2 days	Fri 3/7/03	Tue 3/11/03	8,7	CMS Grad Student												
10	Final Test	2 days	Tue 3/11/03	Thu 3/13/03	9	CMS Grad Student												

Project: CROWBAR Date: Wed 2/19/03	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

CROWBAR

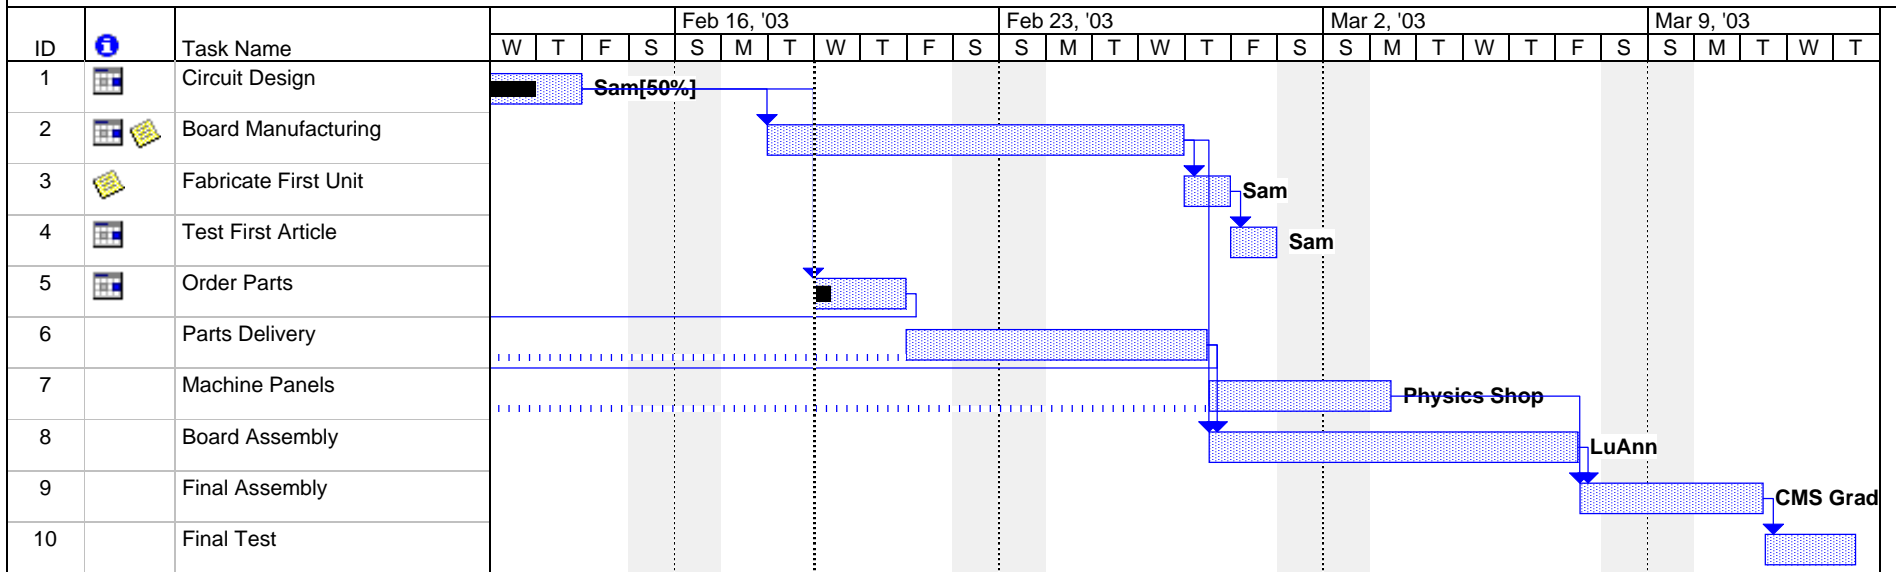

Project: CROWBAR Date: Wed 2/19/03	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

**2 Board Manufacturing**

Advanced Ckts 50 ea @ \$4.37 ea with \$149 setup

**3 Fabricate First Unit**

Sam
